Kaiyo Living
Strictly private and confidential

Riverside Commons Information Memorandum

A$118.0M senior secured construction facility, 9 Marquet Lane, Rhodes NSW

Prepared for prospective senior lenders
Version 1.0, 10 February 2026
Strictly private and confidential
Reference: KL-RC-IM-2026-01
Date: 10 February 2026

Synthetic - for demonstration. All names, entities and figures are fictional.
Confidential. Prepared for the addressee only and not to be relied on by any other party.

Borrower	Riverside Commons Pty Ltd
ABN	91 014 685 765
Registered office	Level 4, 12 Walker Street, Rhodes NSW 2138
Project site	9 Marquet Lane, Rhodes NSW 2138
Sponsor	Kaiyo Living Group Pty Ltd (trading as Kaiyo Living)
Facility sought	A$118.0M senior secured construction facility, staged drawdown, equity first
Date	10 February 2026
Version	1.0
Prepared by	Kaiyo Living Group Pty Ltd, with Corvane Capital Advisory Pty Ltd as sponsor finance adviser
Prepared for	Prospective senior lenders

Document details

Important notice

This information memorandum has been prepared by Kaiyo Living Group Pty Ltd (Kaiyo Living) on behalf of Riverside Commons Pty Ltd (Riverside Commons or the Borrower) to assist prospective lenders to assess a senior secured construction facility. It is not an offer capable of acceptance and does not constitute advice. Pricing and terms are indicative and subject to credit approval, due diligence and documentation.

Forecasts, valuations, costs and programme dates in this document are the estimates of the sponsor and have not been verified by an independent party. A lender will commission its own valuation, quantity surveyor review and legal due diligence, and the findings may differ from the sponsor figures in this document. Recipients should rely on their own enquiries. All figures are in Australian dollars and exclusive of GST unless stated.

1. Executive summary

Riverside Commons is a single-purpose vehicle formed by Kaiyo Living to develop and sell a 162 apartment project at 9 Marquet Lane, Rhodes, on the southern bank of the Parramatta River in the City of Canada Bay local government area. The project comprises two buildings of 11 and 14 storeys above a shared basement of 214 car spaces, with 15,640 sqm of gross floor area and 12,050 sqm of net saleable area.

The Borrower seeks a A$118.0M senior secured construction facility with a 36 month tenor. The facility will refinance the existing A$18.0M land loan and fund construction costs, professional fees, statutory charges, selling costs and capitalised interest and fees. Repayment is from the settlement of apartment sales.

- Site acquired on 14 August 2024 and development consent granted on 20 March 2025 for 162 apartments.
- Fixed price design and construct contract of A$91.2M signed with Tallowood Construction Pty Ltd on 12 December 2025.
- 94 of 162 units (58%) exchanged as at 31 January 2026, with contract value of A$123.6M, which is 1.05 times the facility limit. Purchaser deposits of 10% are held in the sales agent's trust account.
- Sponsor gross realisation value (GRV) of A$228.0M against total development cost (TDC) of A$171.6M, a margin on cost of 32.9%.
- Facility limit equals 51.8% of sponsor GRV and 68.8% of TDC. Sponsor equity of A$53.6M is required, of which A$24.6M has been contributed and A$29.0M will be injected before the first construction draw.
- Practical completion is forecast 24 months from site start, leaving up to 12 months within the 36 month tenor for settlement.

Metric	Sponsor basis
Facility limit	A$118.0M
Total development cost	A$171.6M
Gross realisation value	A$228.0M
Facility to GRV (LVR)	51.8%
Facility to cost (LTC)	68.8%
Margin on cost	32.9%
Presales (units, value)	94 units, A$123.6M
Presales to facility limit	1.05x

Table 1: Headline metrics on the sponsor's figures

2. The facility request

2.1 Indicative terms

Facility type	Senior secured construction facility, staged drawdown, equity first
Limit	A$118.0M
Tenor	36 months from financial close
Margin	3 month BBSW plus 6.50% p.a. on drawn amounts
Establishment fee	1.50% of the limit (A$1.77M)
Line fee	1.25% p.a. on undrawn commitment
Interest	Capitalised during construction
Status	Indicative and subject to credit approval

Indicative terms requested

2.2 Purpose and drawdown

The facility will be applied to refinance the A$18.0M land loan provided by a mid-tier bank at acquisition, and to fund the construction contract, professional fees, statutory charges, selling costs, and capitalised interest and fees. Drawdown is on an equity first basis. The sponsor will inject the remaining A$29.0M of cash equity before the first construction draw. Subsequent draws will be made against progress claims certified by the lender's project monitor.

2.3 Sources and uses

Item	A$M
Land including duty and costs	36.4
Construction contract (Tallowood)	91.2
Professional fees	9.8
Statutory charges and contributions	6.2
Selling and marketing costs	7.0
Finance costs (interest and fees)	15.0
Project contingency	6.0
Total uses (TDC)	171.6
Senior construction facility	118.0
Sponsor equity	53.6
Total sources	**171.6**

Table 2: Sources and uses of funds (sponsor budget)

Sponsor equity of A$53.6M comprises A$24.6M contributed to date and A$29.0M to be injected. Of the contributed amount, A$18.4M funded the balance of the land purchase beyond the land loan and A$6.2M funded pre-development costs. Net debt at 31 December 2025 was A$15.9M, being the A$18.0M land loan less cash held by the Borrower. On the full facility, debt to equity is 2.2 times.

3. Sponsor and Borrower

3.1 Kaiyo Living

Kaiyo Living Group Pty Ltd, trading as Kaiyo Living, is a Sydney based residential developer and the sole sponsor of the project. It controls Riverside Commons, provides development management and has established the project governance described below. Kaiyo Living has other projects in delivery, and lenders should consider the sponsor's liquidity across its whole programme (see section 8).

3.2 The Borrower

Riverside Commons Pty Ltd (ABN 91 014 685 765) is a special purpose company with its registered office at Level 4, 12 Walker Street, Rhodes NSW 2138. It has no operating revenue. Its only material asset is the site and the work in progress. The Borrower will not incur other indebtedness and will not carry on any business other than the project.

3.3 Directors

Director	Role
Daniel Hartigan	Director and Chief Executive Officer, Kaiyo Living
Priya Darby	Director and Chief Financial Officer, Kaiyo Living
Stephen Allardyce	Non-executive Director (sponsor nominee), chair of the development committee

Table 3: Directors of Riverside Commons Pty Ltd

The development committee, chaired by Mr Allardyce, reviews construction progress, cost reports, sales results and variations above agreed thresholds. The sponsor proposes that lender nominated reporting be delivered to this committee monthly.

3.4 Advisers

Role	Firm
Builder	Tallowood Construction Pty Ltd
Sales agent	Bellamy & Roe Projects Pty Ltd
Auditor	Pellett & Wynn Chartered Accountants
Sponsor finance adviser	Corvane Capital Advisory Pty Ltd
Valuer (proposed)	Harcourt Lyle Valuers Pty Ltd (Sydney)
Project monitor (proposed)	Dunmore Fraser Quantity Surveyors Pty Ltd
Lender's counsel (proposed)	Brannock Sutherland Lawyers

Table 4: Project advisers. Proposed appointments are subject to lender approval.

4. The project

4.1 Site and location

The site at 9 Marquet Lane, Rhodes is on the southern bank of the Parramatta River within the City of Canada Bay local government area. Rhodes is an established high density precinct with a railway station, retail and employment nearby. The site was acquired on 14 August 2024 for A$34.2M, or A$36.4M including stamp duty and costs. The sponsor estimates the as-is land value at A$34.5M.

4.2 Development

Development consent was granted on 20 March 2025 for 162 apartments in two buildings of 11 and 14 storeys above a shared basement of 214 car spaces. The mix comprises one, two and three bedroom apartments. The gross floor area is 15,640 sqm and the net saleable area is 12,050 sqm, a net to gross efficiency of 77.0%. Average net saleable area is 74.4 sqm per apartment.

4.3 Project history

Date	Milestone
14 Aug 2024	Site settled, funded by sponsor equity and an A$18.0M land loan
20 Mar 2025	Development consent granted
8 Sep 2025	Sales campaign launched with display suite and agency appointment
12 Dec 2025	Design and construct contract of A$91.2M executed
31 Jan 2026	Presales reach 94 of 162 units (58%)

Table 5: Project milestones to date

5. Construction

Tallowood Construction Pty Ltd will build the project under a fixed price design and construct contract with a contract sum of A$91.2M, equal to approximately A$5,830 per sqm of gross floor area. The sponsor forecasts practical completion 24 months from site start. The contract provides for security of performance by bank guarantees of 5% of the contract sum, or A$4.56M.

The sponsor budget carries a project contingency of A$6.0M outside the contract sum, equal to 6.6% of the contract sum. The sponsor will not permit variations that increase the contract sum without development committee approval and, where required, lender consent. The lender's project monitor will certify each progress claim before drawdown.

The basement will be excavated close to the Parramatta River. Geotechnical, groundwater and contamination investigations have been completed as part of the consent process, and the sponsor will provide the reports to lenders in the data room. Flood planning levels have been addressed in the approved design.

6. Sales and presales

The sales campaign launched on 8 September 2025 and Bellamy & Roe Projects Pty Ltd acts as sales agent. As at 31 January 2026, 94 of 162 units (58%) had been exchanged with a contract value of A$123.6M, an average of about A$1.32M per unit. This is an average of about 20 exchanges a month since launch. Deposits of 10%, being A$12.36M, are held in the agent's trust account.

The remaining 68 units (42%) are unsold. On the sponsor's pricing they represent A$104.4M of the A$228.0M GRV, an average of about A$1.54M per unit. The unsold stock is weighted to higher floors and three bedroom apartments, which the sponsor prices at a premium to the stock sold to date. Lenders should note that the unsold average is 16.7% above the presold average, and that the sponsor's GRV depends on achieving that premium.

Presales of A$123.6M exceed the facility limit by A$5.6M. The sponsor will agree a minimum presales covenant and a minimum release price schedule so that net sale proceeds are applied to the facility until it is repaid in full.

7. Financial analysis

7.1 Returns

On the sponsor's figures, GRV of A$228.0M less TDC of A$171.6M gives a development profit of A$56.4M. This is a margin on cost of 32.9% and a margin on GRV of 24.7%. The facility limit of A$118.0M is 51.8% of GRV and 68.8% of TDC. The sponsor's equity is subordinated to the facility and is exposed first to any shortfall in sales proceeds or increase in cost.

7.2 Sensitivity to realisation value

The table below shows the effect of lower realisations on loan to value and margin on cost, holding TDC at A$171.6M and the facility at A$118.0M. Break-even for the facility alone, before selling costs, is a fall in GRV of 48.2%.

GRV change	GRV (A$M)	LVR	Margin on cost
Base case	228.0	51.8%	32.9%
Minus 5%	216.6	54.5%	26.2%
Minus 10%	205.2	57.5%	19.6%
Minus 15%	193.8	60.9%	12.9%
Minus 20%	182.4	64.7%	6.3%

Table 6: Sensitivity of LVR and margin to GRV (costs unchanged)

7.3 Sensitivity to construction cost

A 10% increase in the construction contract sum (A$9.1M) would lift TDC to A$180.7M and reduce margin on cost to 26.2% on base case GRV. The A$6.0M project contingency would absorb part of this increase before any call on sponsor equity beyond the amounts committed.

7.4 Indicative facility profile

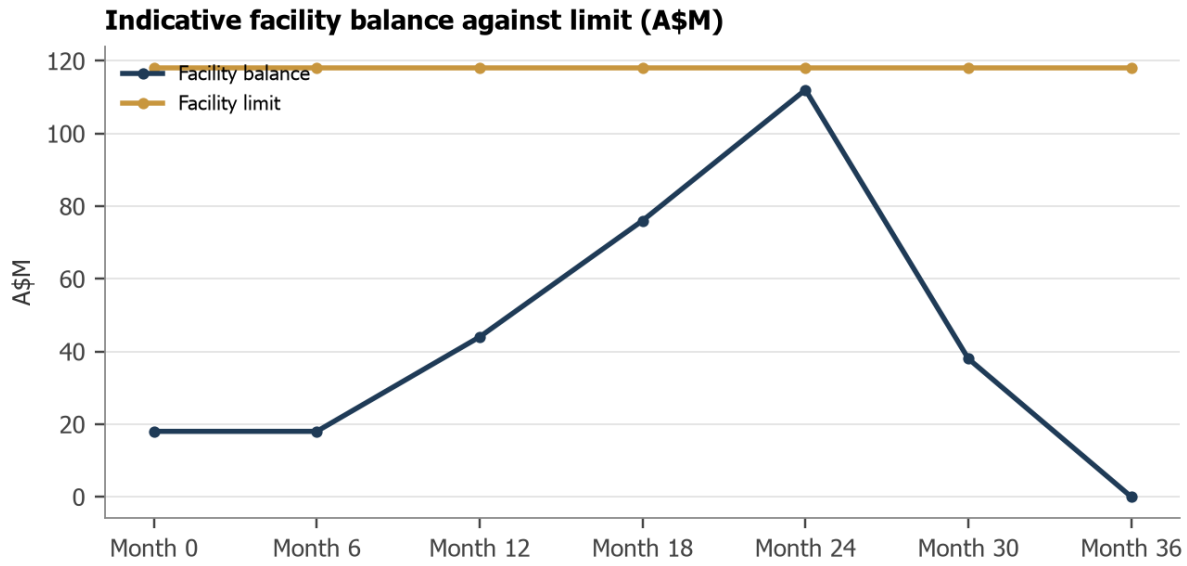


Figure 1: Sponsor forecast of the facility balance. Month 0 is financial close and the 24 month build assumes site start at financial close. Capitalised interest is included.

The profile reflects the equity first requirement, with the balance held at A$18.0M while the sponsor injects its remaining equity. The balance peaks near A$112.0M at practical completion. Settlement of presold units then repays the majority of the facility, with the balance cleared from settlement of unsold stock before month 36.

8. Key risks and mitigants

The sponsor has identified the following principal risks. The figures in this document are the sponsor's estimates, and an independent valuation and quantity surveyor review may produce a lower GRV, a higher cost or a longer programme. The sponsor invites lenders to test each of these items in due diligence.

Risk	Mitigant
Construction cost: provisional sums, contingency and escalation may exceed allowances, and any overrun falls on the sponsor equity cushion	Fixed price contract, A$6.0M contingency, monitor certification, cost to complete test before each draw
Sales and settlement: 68 units (42%) unsold, and purchasers' lenders may value below contract price given supply in Rhodes, Wentworth Point and Olympic Park	58% presold, 10% deposits in trust, minimum presales and release price covenants
Programme: delay shortens the settlement window within the 36 month tenor and increases capitalised interest	Liquidated damages, long stop date, monitor reporting, interest allowance in TDC
Builder counterparty: lump sum contract above A$90M and builder insolvency is a recurring sector risk in NSW; performance security is limited to 5% bank guarantees	Builder financial review, step in rights, monitor oversight, assignment of contract
Site and environment: proximity to the Parramatta River and a former industrial precinct, with flood levels, groundwater and possible residual contamination	Completed investigations, flood compliant design, contingency, specialist consultants
Sponsor equity: A$29.0M of cash equity remains to be injected before the first construction draw, and other sponsor projects compete for liquidity	Equity first condition precedent, sponsor liquidity reporting, completion guarantee

Table 7: Principal risks and mitigants

9. Security and repayment

9.1 Proposed security

- First ranking registered mortgage over the site at 9 Marquet Lane, Rhodes.
- General security agreement over all present and after acquired property of Riverside Commons Pty Ltd.
- Assignment of the design and construct contract, bank guarantees, consultant warranties, insurances and sales contracts.
- Fixed charge over the project accounts and deposits released from trust.
- Sponsor completion guarantee and cost overrun undertaking from Kaiyo Living Group Pty Ltd.
- Subordination of all sponsor and related party loans.

9.2 Repayment

Repayment will come from settlement proceeds. Net proceeds of each settlement, after agent commission and permitted costs, will be applied to the facility until it is repaid in full. The sponsor expects practical completion 24 months from site start, with settlement of presold units shortly after completion and the remaining stock settling within the 36 month tenor. Any extension would require lender consent.

10. Proposed covenants and conditions

10.1 Financial and undertakings covenants

- Facility limit not to exceed 70% of TDC, tested on each drawdown.
- Minimum presales cover of 100% of the outstanding facility, maintained through construction.
- Minimum release price for each unit, agreed with the lender before settlement.
- Cost to complete test on each drawdown, with any shortfall funded by sponsor equity.
- Practical completion by a long stop date to be agreed.
- Monthly reporting of construction progress, cost, sales and variations, and quarterly sponsor liquidity reporting.

10.2 Conditions precedent

- Satisfactory independent valuation, quantity surveyor review and legal due diligence.
- Execution of facility and security documents, and registration of the mortgage.
- Evidence of sponsor equity of A$24.6M contributed, and injection of the remaining A$29.0M before the first construction draw.
- Executed design and construct contract, bank guarantees and builder insurances.
- Copies of sales contracts for all presold units and confirmation of deposits in trust.
- Payout and release of the existing A$18.0M land loan.

11. Process and sign-off

Prospective lenders are invited to provide indicative terms, subject to credit approval and due diligence. Enquiries should be directed to Corvane Capital Advisory Pty Ltd or to Ms Venkataraman at Kaiyo Living. A data room containing the consent, contract, sales register and site reports will be made available to parties who sign a confidentiality undertaking.

Role	Name	Date
Director and CEO, Kaiyo Living	Daniel Hartigan	10 Feb 2026
Director and CFO, Kaiyo Living	Priya Darby	10 Feb 2026
Non-executive Director, development committee chair	Stephen Allardyce	10 Feb 2026

Table 8: Approval for release of this information memorandum
